

PROJECT CHARTER

COSUP Website & Mobile Application

Community Oriented Substance Use Programme

Prepared By	The 5 Watermelons Zandile Selao Tshiamo Mosetlha Matlhogonolo Keebine Muhluri Nkuna Ndabezinhle Mathunyane
Module	DISD0601 / XISD5319 — Work Integrated Learning
Institution	IIE Rosebank College, Pretoria CBD
Client Organisation	Community Oriented Substance Use Programme (COSUP)
Date	13 March 2026
Version	1.0 — Initial Release

1. Introduction

1.1 Purpose of the Project Charter

This Project Charter formally authorises and defines the COSUP Website & Mobile Application project, undertaken by The 5 Watermelons as part of the DISD0601/XISD5319 Work Integrated Learning module at IIE Rosebank College, Pretoria CBD.

The purpose of this document is to establish a shared understanding of the project among all stakeholders — the student development team, the academic institution, and the client organisation. It defines the project's objectives, scope, deliverables, schedule, budget, risks, and organisational structure, serving as the authoritative reference point for all project decisions throughout the development lifecycle.

The Community Oriented Substance Use Programme (COSUP) is the client organisation for which the system is being developed. COSUP is a collaborative public health initiative established in 2015 between the City of Tshwane and the University of Pretoria's Department of Family Medicine. It provides free, harm reduction-based services to people who use drugs in the Tshwane metropolitan area, including Opioid Agonist Therapy, Needle and Syringe Programmes, Psychosocial Support, Vocational Training, HIV and HCV Prevention, and Community Integration services.

The system being developed consists of two complementary digital platforms: a responsive public-facing website and an Android mobile application. Both platforms are designed to provide an accessible, confidential, and multilingual gateway for individuals seeking harm reduction services and information in Tshwane.

By signing this charter, all parties acknowledge their roles and responsibilities, agree to the defined scope of work, and commit to working collaboratively toward the successful and timely delivery of the project within the constraints of the academic programme.

2. Project and Product Overview

The COSUP Website & Mobile App project aims to address a significant and long-standing gap in COSUP's service delivery infrastructure: the complete absence of a dedicated digital presence. Despite more than a decade of continuous operation and having supported in excess of 5,000 individuals across Tshwane, COSUP has until now relied exclusively on physical outreach, peer networks, and word-of-mouth referrals to connect people with its services.

The project will deliver two integrated digital products:

- A Responsive Website — a comprehensive, public-facing information platform built using ASP.NET MVC and C#, providing detailed and accessible information about COSUP's mission, services, clinic locations, impact statistics, and organisational history. The website is designed for broad public audiences, including prospective clients, partner organisations, funders, and the general public.
- An Android Mobile Application — a dynamic, interactive application developed using Kotlin in Android Studio, specifically designed for community members and individuals seeking immediate access to help. Key features include a one-tap crisis support channel (the Hopeline), an interactive clinic and service point locator, and a news and updates feed.

Both platforms will be developed with COSUP's core mission at the centre: harm reduction, human rights, and community dignity. Neither platform will collect, store, or process sensitive health information. The platforms function strictly as public-facing information and communication tools.

A defining feature of the platform is full multilingual support across seven South African languages — Xitsonga, TshiVenda, IsiZulu, SeTswana/Sepedi, Afrikaans, Xhosa, and English — ensuring that language is never a barrier to accessing life-saving services across the linguistically diverse communities of Tshwane.

The technology stack comprises C# and ASP.NET MVC for the web backend, Kotlin for Android mobile development, and Microsoft SQL Server for database management, with development conducted in Visual Studio 2022 and Android Studio respectively.

The project is formally supervised through the XISD5319 Work Integrated Learning module at IIE Rosebank College, with all deliverables subject to academic oversight and evaluation.

3. Justification

3.1 Business Need

COSUP has operated for over ten years without a dedicated digital platform. In the absence of a centralised online presence, individuals seeking services have historically depended on physical encounters with outreach workers, referrals from other health facilities, peer networks, and community notices. While these mechanisms have enabled COSUP to reach more than 5,000 people since its establishment, they are inherently limited in reach, consistency, and scalability across a large metropolitan area.

The absence of a digital presence creates several critical operational gaps. First, it limits COSUP's ability to reach individuals who are not already embedded in peer networks or connected to public health facilities, particularly those in geographically dispersed areas such as Mamelodi, Soshanguve, and other townships across Tshwane. Second, it results in missed crisis intervention opportunities: when an individual is ready to seek help, their most likely first action is to search online. Without a digital footprint, COSUP is entirely absent from this crucial, time-sensitive moment. Third, information about clinic operating hours, service availability, and programme updates is fragmented and inconsistent, relying on physical notices that may be outdated or inaccessible.

The present moment is particularly opportune for the development of this platform. Smartphone penetration and mobile data usage in South Africa have grown substantially, making a mobile application the most effective and direct means of reaching broad and underserved populations. After ten years of proven operation, COSUP has a well-established service model and a clear understanding of community needs — a digital platform represents the logical next step in scaling its impact for a second decade of service. Furthermore, as a nationally and internationally recognised harm reduction programme, a professional digital presence is commensurate with COSUP's standing and would formalise its public communications in a manner befitting an organisation of its stature.

3.2 Public Health and Business Impact

The COSUP digital platform is anticipated to generate significant positive impacts across multiple dimensions of public health and organisational effectiveness.

From a public health perspective, the platform is expected to increase the uptake of COSUP's free services by making information readily available to a far wider audience. Improved access to clinic locations and service descriptions will facilitate earlier engagement with Opioid Agonist Therapy, Needle and Syringe Programmes, and HIV and HCV prevention services, directly contributing to a reduction in the transmission of blood-borne infections among people who inject drugs. The confidential and discreet nature of a digital platform is expected to lower the psychological barrier to seeking help, enabling individuals to access information privately and without the fear of stigma or public identification, thereby encouraging earlier and more sustained engagement with health services. The Hopeline feature — a prominently accessible, one-tap connection to COSUP's crisis

support line — offers a low-threshold intervention channel that could meaningfully reduce harm during acute crisis episodes.

Beyond the immediate user population, the platform offers substantial broader benefits. For COSUP as an organisation, a professional multilingual digital platform will reinforce its credibility and strengthen relationships with funders, partners, and the City of Tshwane. For the University of Pretoria's Department of Family Medicine, the platform provides a tangible, technology-enabled community engagement tool and a potential model for research dissemination and anonymised service demand analysis. At a policy level, a well-documented, tech-enabled harm reduction model can serve as a powerful advocacy instrument, providing concrete evidence for other municipalities and national government stakeholders seeking to scale or replicate COSUP's approach. The platform also contributes indirectly to reducing the burden on general public healthcare facilities by directing a specialised population to dedicated, rights-based services equipped to meet their unique needs.

These anticipated impacts are grounded in COSUP's documented track record: over ten years of operation, 5,000 or more people supported, and recognition as a pioneering domestic harm reduction programme. The platform's potential to amplify this reach through digital accessibility represents a compelling public health investment.

4. Scope

4.1 Objectives

The following objectives define the measurable outcomes the project is committed to delivering:

1. **Develop a Professional Digital Presence:** To design, build, and deploy a fully functional, responsive website and Android mobile application that accurately represents COSUP's brand, mission, and services.
2. **Implement a Multilingual Interface:** To integrate full user interface and content support for seven South African languages — Xitsonga, TshiVenda, IsiZulu, SeTswana/Sepedi, Afrikaans, Xhosa, and English — ensuring the platform is accessible to the diverse communities of Tshwane.
3. **Create an Accessible Service and Clinic Locator:** To develop a feature enabling users to locate nearby COSUP service points, displaying essential information including clinic name, distance, address, and operating hours.
4. **Establish a Direct Crisis Support Channel (Hopeline):** To implement a prominent, one-tap feature within the mobile application that connects individuals in crisis directly to COSUP's support line via call or WhatsApp.
5. **Ensure Full Data Privacy and Regulatory Compliance:** To build the platform in accordance with the Protection of Personal Information Act (POPIA, Act 4 of 2013), ensuring no sensitive health data is stored and that all user data is handled with explicit consent, encryption, and full user rights to access, correct, or delete their information.
6. **Deliver a Complete, Documented Handover Package:** To provide COSUP with fully documented source code and a comprehensive Maintenance and Handover Guide, enabling the organisation to manage the platform independently after the student team's formal involvement concludes.

4.2 High-Level Requirements

Functional Requirements

The following functional requirements define what the system must be capable of performing:

Ref	Requirement	Description
FR1	Public Information Display	The system must present clear information about COSUP's mission, history, partnerships, and impact statistics.
FR2	Service Listings	The system must list all core COSUP services with descriptions: Opioid Agonist Therapy, Needle & Syringe Programme, Psychosocial Support, Vocational Training, HIV & HCV Prevention, and Community Integration.
FR3	Multilingual Support	The system must allow users to switch the interface language among the seven identified South African languages.
FR4	Clinic/Service Point Locator	The system must allow users to search for and view nearby COSUP clinics and outreach points, displaying address, distance, and operating hours.
FR5	Hopeline Access	The mobile application must provide a consistently visible, one-tap button to immediately call or WhatsApp the COSUP support line.
FR6	News and Updates	The system must include a section for displaying latest announcements, events, and news items.
FR7	Content Management	The system must include a secure, role-based admin interface for authorised COSUP staff to update clinic hours, news items, and service details.
FR8	Self-Referral Form	The system must include an online form for potential clients to submit contact requests, collecting minimum necessary information with a POPIA-compliant consent mechanism.

Non-Functional Requirements

The following non-functional requirements define how the system must perform:

Ref	Category	Requirement
NFR1	Platform Compatibility	The mobile app must target Android. The website must be responsive across all modern desktop and mobile browsers.
NFR2	Performance	Interfaces should load within 3 seconds on standard broadband/4G connections.
NFR3	Security — Encryption	All data transmission must be secured using HTTPS/TLS encryption.
NFR4	Security — Data Privacy	No sensitive health data (e.g., HIV status, OAT status) shall be stored on the client device or backend.
NFR5	Regulatory Compliance	The system must be fully compliant with POPIA (Act 4 of 2013), including user consent, data access, correction, and deletion provisions.
NFR6	Access Control	Administrative functions must be protected by secure, role-based access control.
NFR7	Usability	The interface must be intuitive and easy to navigate for users with varying levels of digital literacy.
NFR8	Maintainability	All source code must be well-documented to facilitate future updates and maintenance by COSUP or a third-party developer.


NFR9	No Third-Party Tracking	No third-party analytics or tracking tools shall be embedded without COSUP's explicit prior approval.
------	--------------------------------	---

4.3 Major Deliverables

The following major deliverables will be produced throughout the project lifecycle in a structured and sequential manner:

- 1. Project Charter Document**
A formal document outlining the project's purpose, scope, stakeholders, risks, and overall development plan.
- 2. Requirements Analysis Documentation**
A detailed specification of COSUP's functional and non-functional requirements, based on stakeholder engagement and organisational analysis.
- 3. UI/UX Design Prototype**
A high-fidelity interactive prototype representing the system's user interface and experience, refined through feedback from COSUP management.
- 4. Project Plan Documentation**
A comprehensive planning document including the Work Breakdown Structure (WBS), Gantt Chart, PERT Chart, schedule, and resource allocation.
- 5. Web Application (Frontend and Backend)**
A fully functional responsive website developed using ASP.NET MVC and C#, providing public access to COSUP's services, information, and resources.
- 6. Mobile Application (Android)**
A functional Android application developed using Kotlin, enabling users to access COSUP services, clinic locations, and crisis support features.
- 7. Multilingual Implementation Deliverable**
The integration of seven South African languages across both the website and mobile application to ensure accessibility and inclusivity.
- 8. System Testing and Quality Assurance Report**
Documentation of all testing activities, including functional testing, usability testing, and User Acceptance Testing (UAT), along with identified issues and resolutions.
- 9. Final Working System**
A complete, tested, and fully functional website and mobile application ready for handover to COSUP.
- 10. Documentation and Handover Package**
A comprehensive package including source code, technical documentation, and a Maintenance and Handover Guide for COSUP.
- 11. Final Presentation and Demonstration**
A formal presentation demonstrating the completed system to COSUP management and academic evaluators.

4.4 Work Breakdown Structure (WBS)

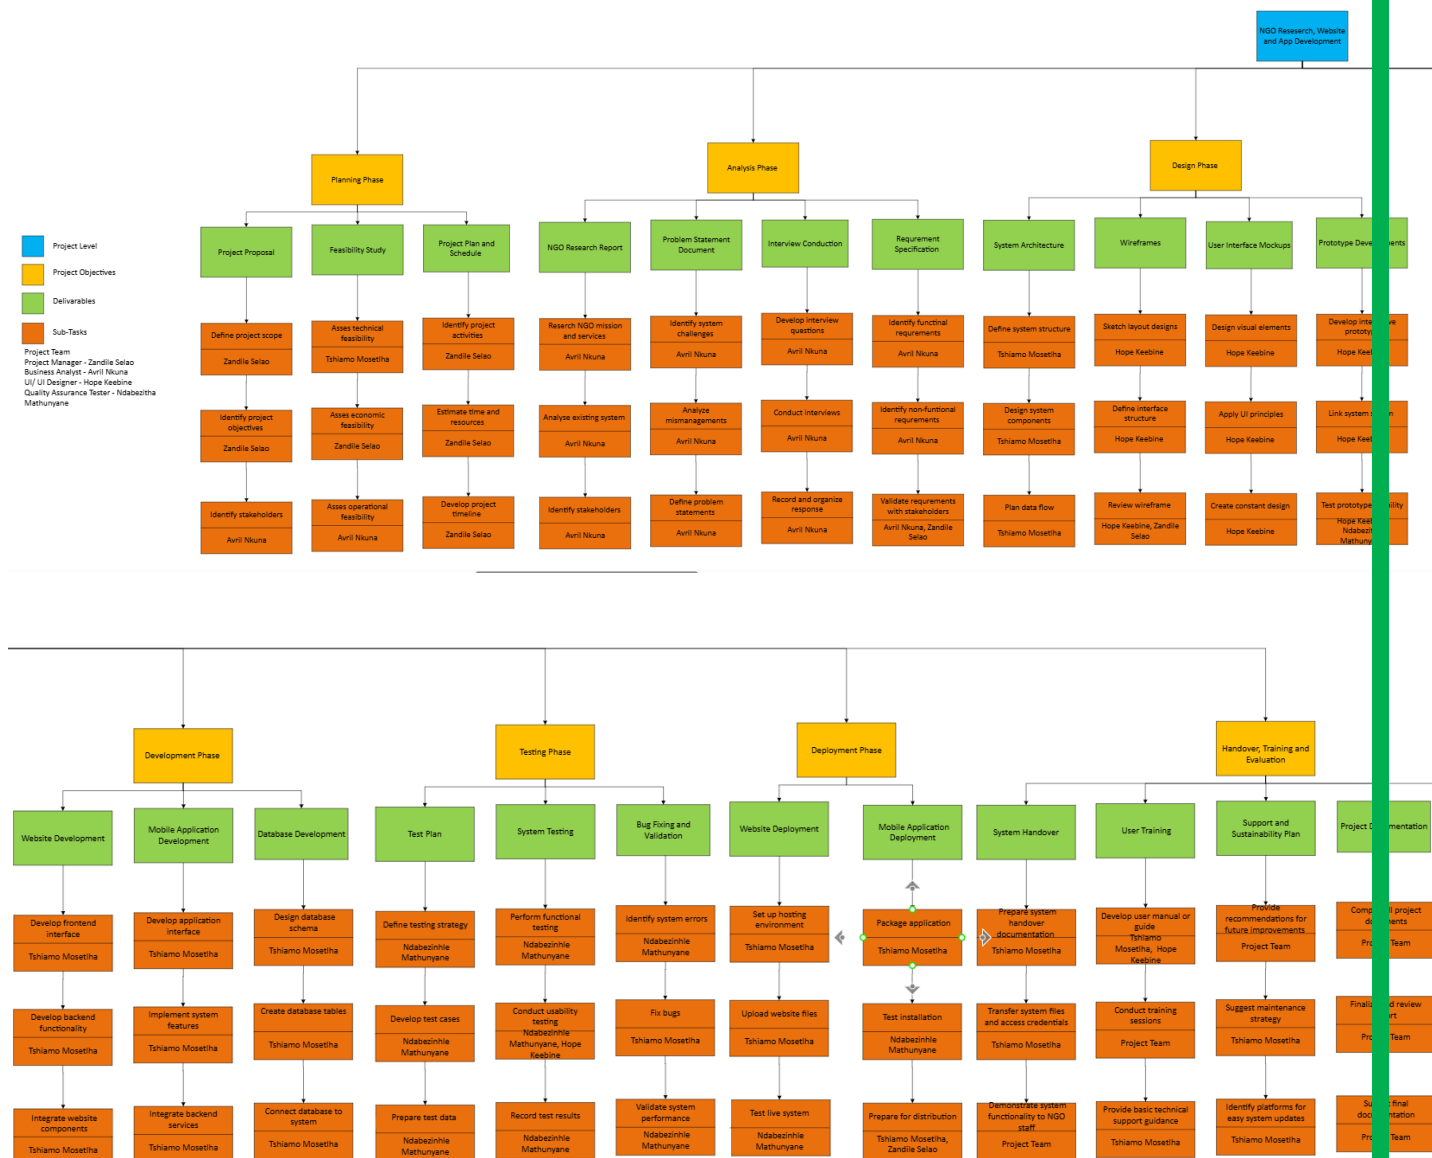

The Work Breakdown Structure (WBS) provides a structured and hierarchical decomposition of all work required to successfully deliver the COSUP Website and Mobile Application project. It translates the project scope into clearly defined phases, deliverables, and tasks, enabling effective planning, task allocation, monitoring, and control throughout the project lifecycle.

5 Items Explicitly Out of Scope

To maintain focus and ensure successful delivery within the academic timeline, the following items are explicitly excluded from the project scope:

- **Patient Record Management:** The system will not store, manage, or process electronic health records, clinical notes, or individual patient treatment data.

- **Storage of Sensitive Health Data:** No sensitive personal health information (such as HIV status, HCV status, or OAT medication details) will be collected or stored.
- **Appointment Booking Functionality:** The system will not include a feature for scheduling or managing appointments with COSUP staff or counsellors.
- **iOS Mobile Application:** The initial development phase focuses exclusively on Android. An iOS version is not planned for this project.
- **Real-Time In-App Chat:** A live, in-app text-based chat feature is not included. The Hopeline provides a direct call/WhatsApp link only.
- **User Accounts and Profiles:** The platform will not require users to create personal accounts or maintain persistent profiles.
- **Long-Term Maintenance and Hosting:** The team's responsibility concludes upon delivery of the completed, documented source code and handover guide. Ongoing hosting, server management, and content updates are the responsibility of COSUP.



6. Project Schedule



6.1 Project Phases and Milestones


The project commenced in mid-February 2026 and is structured into five sequential phases, with two fixed academic submission deadlines: Part 1 (Project Plan) due 23 April 2026, and the Final Submission due 13 May 2026. The following table summarises the project phases, their deliverables, current status, and key sub-tasks.

Phase	Deliverable	Status	Key Sub-Tasks & Milestones
1	Organisation Analysis	Complete	Background research on COSUP; stakeholder needs analysis; initial client engagement and relationship establishment.
2	UI/UX Prototype	Complete — Needs Updates	Wireframe creation; high-fidelity interactive prototype (tmosetlha.github.io/cosup-prototype); presentation to COSUP; incorporation of management feedback.
3	Project Plan (Task 1)	In Progress	Formalise Project Charter; define WBS; create Gantt Chart and PERT Chart; draft budget estimate. Milestone: Project Plan submission — 23 April 2026.
4	Full Development & Testing	Upcoming	Environment setup; ASP.NET MVC backend development; Kotlin Android app development; multilingual integration; security testing; User Acceptance Testing (UAT) with COSUP.
5	Handover & Final Submission	Upcoming	Code documentation; Maintenance and Handover Guide creation; final presentation; source code handover to COSUP. Milestone: Final submission — 13 May 2026.

6.2 Gantt Chart

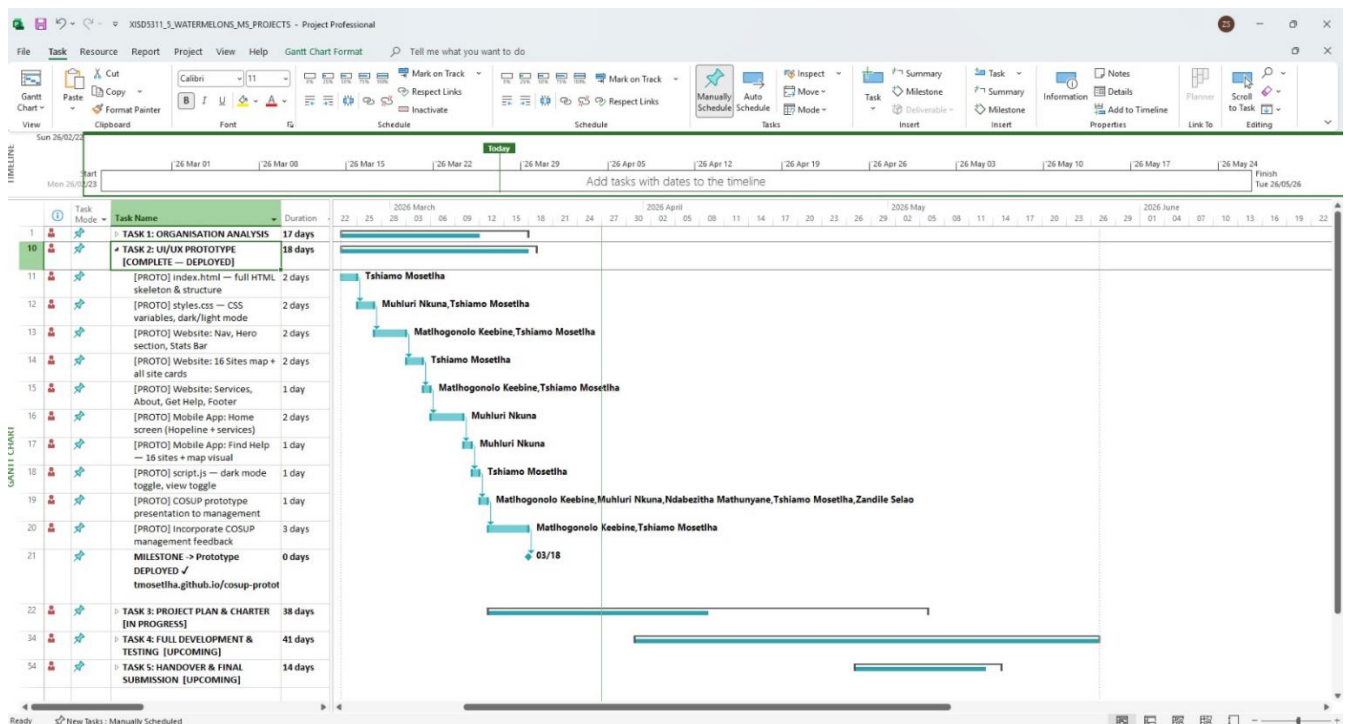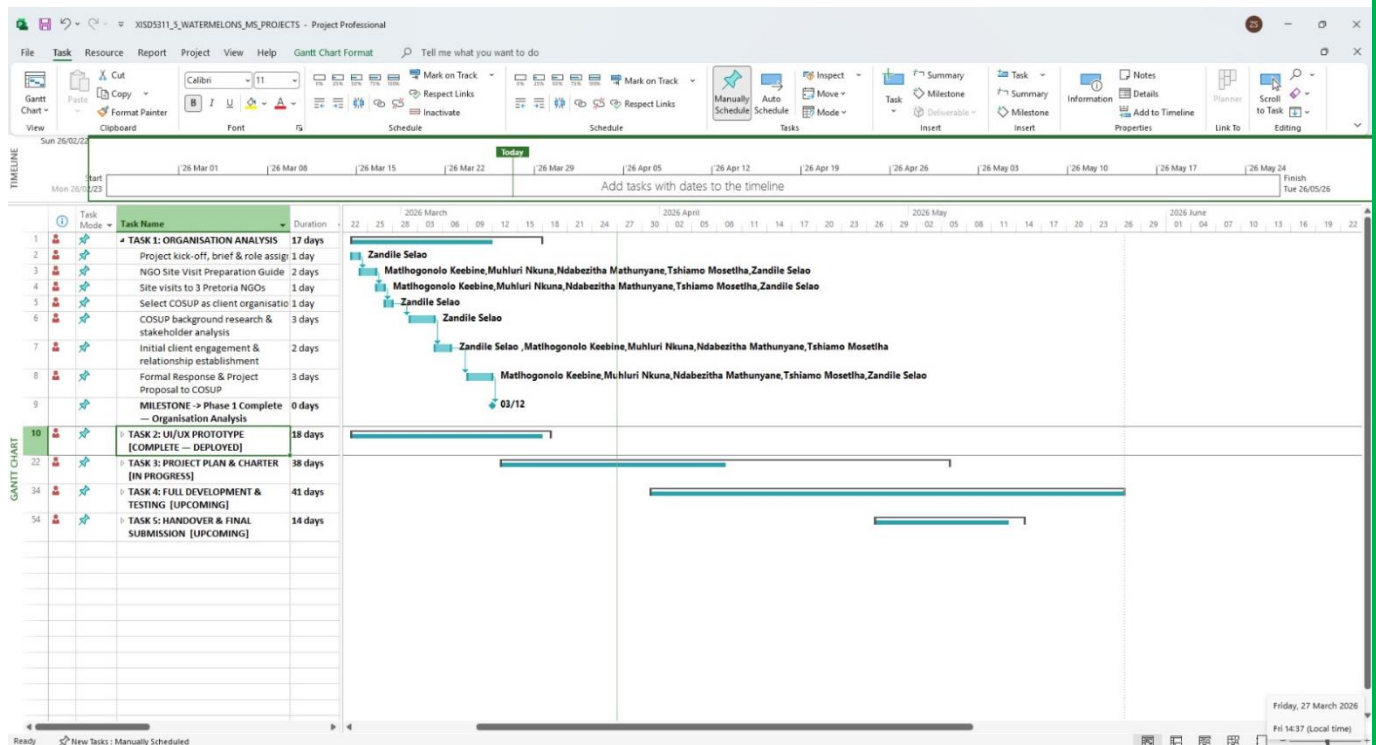


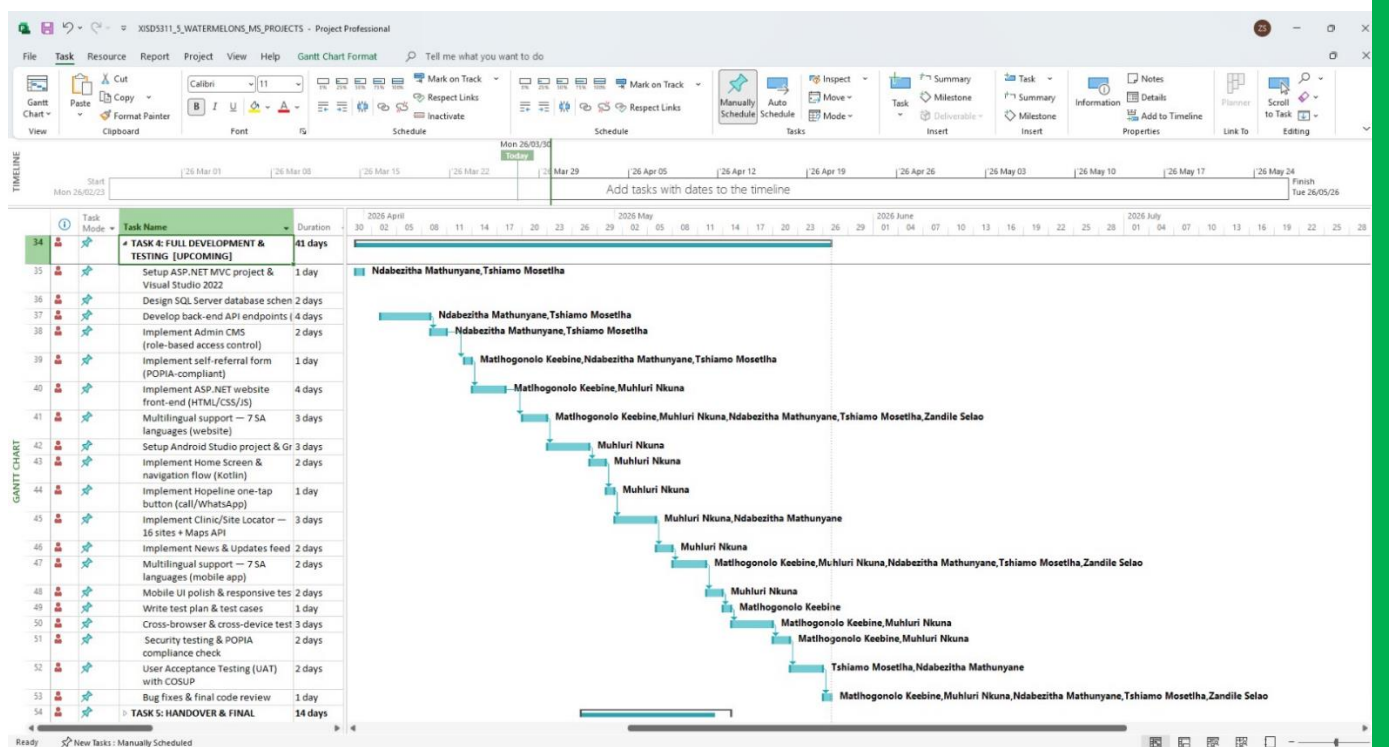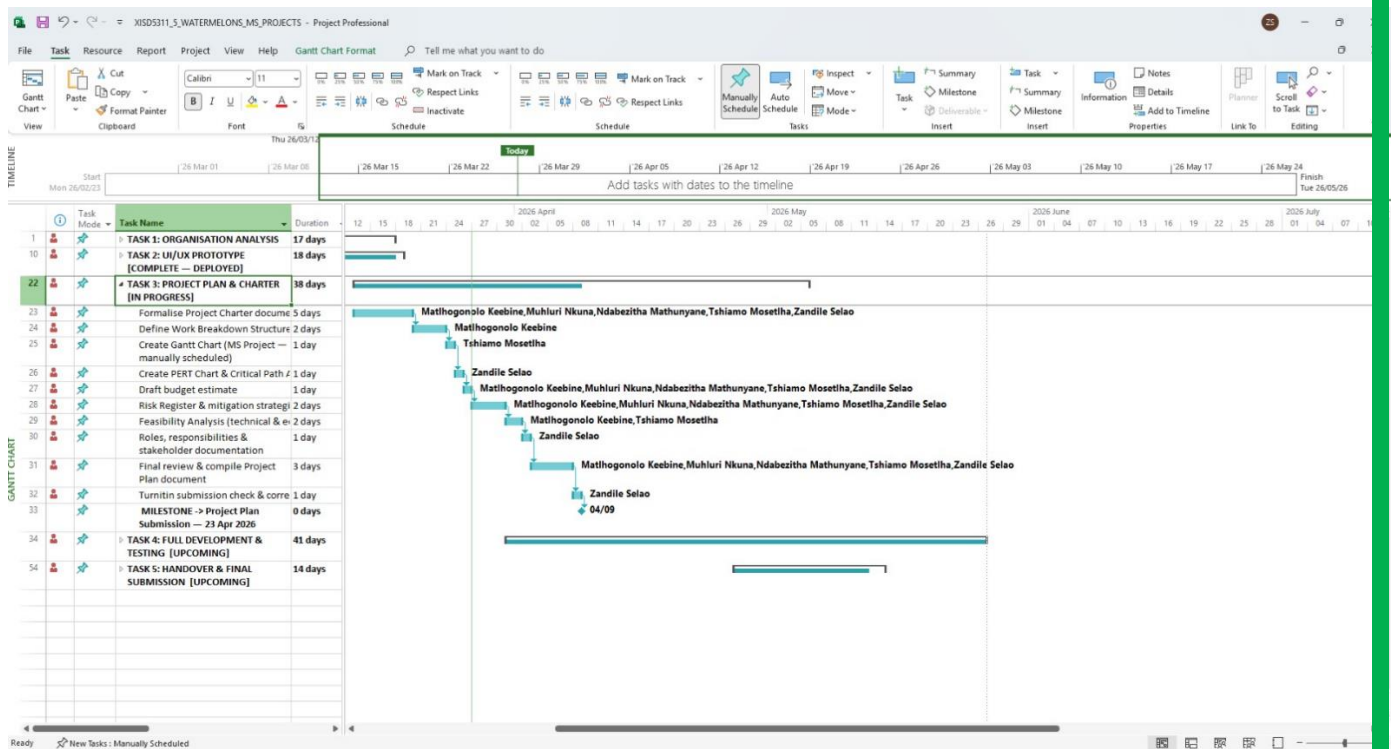

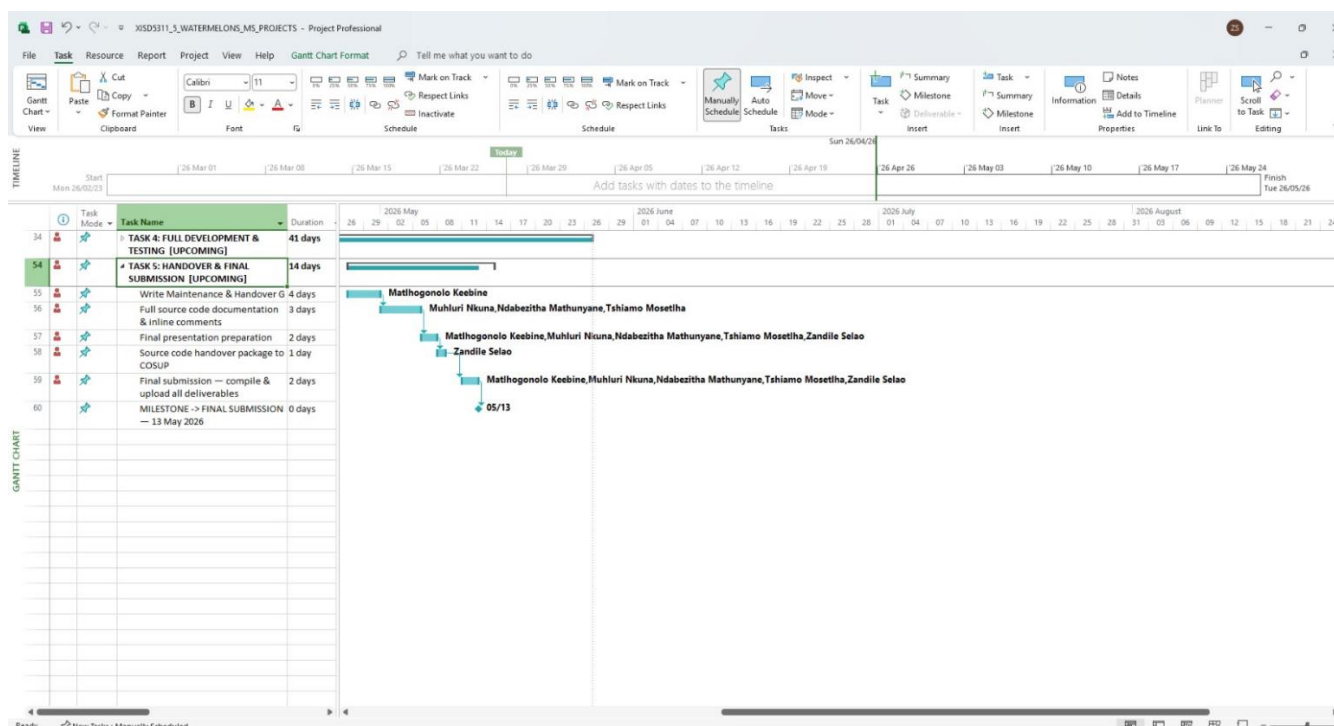

The detailed Gantt Chart, showing individual task durations, assigned responsibilities, and dependencies plotted against the project timeline (mid-February 2026 to 13 May 2026), is to be completed following a team planning session. Tasks must be broken down from the phase-level structure above, durations estimated, and all work mapped backwards from the two fixed submission deadlines. The completed Gantt Chart must be inserted here prior to final submission.

6.3 PERT Chart and Critical Path Analysis

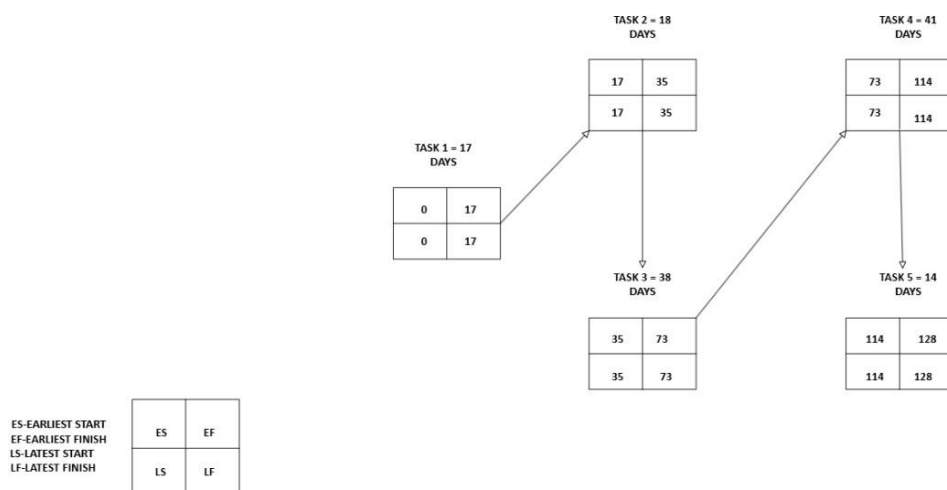

The Programme Evaluation and Review Technique (PERT) network diagram and Critical Path analysis are to be completed following the Gantt Chart exercise. The PERT chart must map all project tasks as nodes, with arrows representing dependencies. The Critical Path — the longest sequence of dependent tasks that determines the minimum project duration — must be identified

and highlighted. Any task on the critical path carries the highest schedule risk, as any delay will directly delay the project's final delivery date. The completed PERT Chart and its interpretation must be inserted here prior to final submission.

7. Budget Estimate

7.1 Funding Source

This project is primarily self-funded by the student development team, The 5 Watermelons. No dedicated monetary budget has been allocated by IIE Rosebank College or COSUP for the development phase. Any out-of-pocket expenses — such as transportation to client meetings, printing of documentation, communication costs, or initial hosting fees — will be borne by the team members personally.

Significant in-kind contributions form the backbone of the project's resource base. IIE Rosebank College provides students with access to academic or free versions of necessary software, including Microsoft Visual Studio 2022 (via academic licensing or the free Community Edition) and Microsoft SQL Server (Developer Edition). Android Studio and the Kotlin programming language are freely available as open-source tools. COSUP will contribute essential in-kind resources, including official branding assets, approved and vetted content, the confirmed Hopeline contact details, and staff time for providing domain expertise, prototype review, and user acceptance testing feedback.

7.2 Budget Estimate

The following table presents the estimated project budget. Items available at no cost are noted accordingly. Cells marked [Team to Insert] require confirmation and population following a team budget discussion session.

Category	Item	Est. Cost (ZAR)	Notes
Software & Tools	Visual Studio 2022	R 0.00	Student/Community Edition
	Android Studio	R 0.00	Open-source, free
	SQL Server Developer Edition	R 0.00	Free for development
	Microsoft Office 365	R 0.00	College student licence
Hosting & Infrastructure	Web Server Hosting (e.g., Azure)	R 70 000.00	Est. first 3–6 months
	Production Database Hosting	R 50 000.00	Often bundled with web hosting
	Custom Domain Name (cosup.org.za)	R 20 000.00	Est. R100–R200/year
Travel & Meetings	Transport to COSUP offices	R 10.00	Return trips, Tshwane
Documentation	Printing (reports, final documents)	R 2.00	Draft and final copies
Communication	Airtime/Data for client calls	R 1000 .00	Team communication with COSUP
Contingency	Unforeseen expenses (10% buffer)	R 10.00	10% of non-zero line items
TOTAL ESTIMATED PROJECT BUDGET		R141 022	

Note: The estimated commercial value of this project, if procured from a professional software development agency, is conservatively estimated at between R265,000 and R505,000. This figure encompasses business analysis, UI/UX design, full-stack development, project management, quality assurance, and documentation. This estimate underscores the significant value that this academic collaboration delivers to COSUP at no direct development cost to the organisation.

8. Assumptions, Constraints, Risks and Risk Management

8.1 Assumptions

The following assumptions are the conditions believed to be true for the duration of the project. If any assumption proves incorrect, the project plan may require revision.

Ref	Assumption
A1	COSUP will provide all necessary branding assets (logo, colour palette, style guide) and approved content (service descriptions, clinic details, Hopeline number) in a timely manner as requested.
A2	Each team member has access to a functioning personal laptop or computer capable of running Visual Studio 2022 and Android Studio.
A3	IIE Rosebank College will continue to provide access to academic software licences for the duration of the project.
A4	COSUP will designate a single point of contact who is available for regular communication and timely feedback throughout the project lifecycle.
A5	Internet connectivity will be sufficiently reliable for all team members to conduct research, communicate, and utilise cloud-based development tools.
A6	COSUP management supports this collaboration and understands that this is a student academic project with defined limitations and a fixed end date.

8.2 Constraints

The following constraints represent the hard limitations and boundaries within which the project must operate.

Ref	Constraint Type	Description
C1	Time	Fixed, non-negotiable academic submission deadlines: Part 1 (Project Plan) due 23 April 2026; Final Submission due 13 May 2026.
C2	Budget	No dedicated monetary fund exists. All costs are self-funded by team members personally.
C3	Team Size	The project is limited to five members with concurrent academic commitments, restricting total available working hours.
C4	Technology Stack	The project is committed to the selected stack: C# / ASP.NET MVC (web), Kotlin (Android), SQL Server (database). Pivoting to alternative technologies is not feasible within the academic timeline.
C5	Legal — POPIA	The project must comply fully with POPIA (Act 4 of 2013). No sensitive health data may be collected or stored under any circumstances.
C6	Scope	The project scope is strictly limited to the features defined in Section 4. Items listed as out of scope may not be introduced without a formal change control process.
C7	Handover	The team's formal involvement concludes on 13 May 2026. No long-term maintenance or support can be provided beyond this date.

8.3 Risk Register

The following risk register identifies potential events that could negatively impact the project, along with their assessed likelihood and potential impact.

Ref	Category	Risk Description	Likelihood	Impact	Priority
R1	Technical	Multilingual integration proves more complex than anticipated, causing development delays.	Medium	High	High
R2	Technical	Hosting environment has compatibility issues with the ASP.NET application or SQL Server database.	Low	High	Medium
R3	Technical	A security vulnerability is discovered late in development, requiring major rework to ensure POPIA compliance.	Low	High	Medium
R4	Team	A key team member becomes unavailable due to illness, personal emergency, or withdrawal from the module.	Medium	High	High
R5	Team	A critical skill gap (e.g., Kotlin development, database hosting) is identified and slows progress.	Medium	Medium	Medium
R6	Client	COSUP's point of contact is unresponsive or slow to provide feedback, delaying prototype updates and UAT.	Medium	High	High
R7	Client	COSUP requests significant scope changes that cannot be accommodated within the academic timeline.	Low	Medium	Low
R8	Client	COSUP fails to provide required branding assets and approved content by the date needed to begin development.	Medium	High	High
R9	Schedule	A development phase takes longer than estimated, pushing subsequent phases past the final deadline.	Medium	High	High
R10	Legal	Inadvertent collection or storage of data that violates POPIA, resulting in legal and ethical breach.	Low	Critical	High
R11	External	The public GitHub prototype link contains outdated or incorrect information that misrepresents COSUP.	Low	Medium	Low

8.4 Risk Management and Mitigation Strategies

Ref	Mitigation Strategy
R1	Develop a proof-of-concept for language switching early in Phase 4. Allocate schedule buffer specifically for this feature. Use established localisation libraries where available.
R2	Research and select a hosting provider early in Phase 4. Establish a staging environment mirroring the production environment to test compatibility well before the final deadline.
R3	Adopt a security-first development approach. Conduct regular code reviews with a security focus. Adhere strictly to the principle of storing no sensitive data. Perform vulnerability scanning throughout development.
R4	Ensure knowledge is shared across the team through cross-training and up-to-date documentation. No feature should be understood by only one member. Communicate availability issues promptly.
R5	Identify skill gaps early and allocate time for focused learning, online resources, and pair programming. Leverage team members' complementary strengths.
R6	Establish agreed response time expectations with the COSUP contact at project outset. Schedule feedback sessions proactively. Escalate delays to the academic supervisor if necessary.
R7	Reiterate the agreed scope to COSUP at each milestone. Frame new requests as candidates for future development phases. Obtain formal scope sign-off from COSUP early in Phase 3.
R8	Request all branding assets and content from COSUP immediately upon project plan approval. Build placeholder content into the prototype and send timely reminders as deadlines approach.
R9	Maintain a detailed Gantt Chart with realistic task estimates and built-in buffer time. Track progress weekly and flag any slippage immediately to enable prompt replanning.
R10	Make POPIA compliance a non-negotiable design requirement from the outset. The core principle of storing no sensitive health data is the primary control. All form submissions will include explicit consent mechanisms.
R11	Use a private repository for active development. Clearly mark the public prototype as a prototype. Before handover, confirm that all sensitive or placeholder content has been removed from public-facing versions.

9. Feasibility Analysis

9.1 Technical Feasibility

The project is assessed as technically feasible. The team possesses a solid foundational skillset in the core technologies required for delivery, with areas of developing proficiency that are appropriate for a final-year student project operating within an academic learning context.

Skill Area	Proficiency Level	Notes
C# / ASP.NET MVC	Strong / Developing	Core framework taught in the programme; foundational knowledge is strong.
Kotlin / Android Studio	Developing	Part of the curriculum; will require focused effort and peer learning.
Front-End Web (HTML, CSS, JavaScript)	Strong	Demonstrated competency through the existing prototype.
Database Design (SQL Server)	Strong / Developing	Simple content and form schema is achievable. Complex relationships are not required.
Multilingual Implementation	Developing	Known technical challenge; early prototyping and localisation libraries will be utilised.
API Integration (Maps/Clinic Locator)	Developing	Third-party mapping API (e.g., Google Maps, OpenStreetMap) integration requires early research.
Security & POPIA Compliance	Developing	Principles understood; correct implementation requires careful code review and testing.
DevOps / Deployment	Developing	Deployment to a live hosting environment is a skill to be developed. Early staging environment setup is critical.

The chosen technologies are appropriate and proven for this type of project. ASP.NET MVC with C# is a mature, secure, and industry-standard framework for public-facing web applications. Kotlin is Google's preferred language for Android development, offering modern syntax and robust tooling. SQL Server is a reliable, industry-standard database system that integrates seamlessly with ASP.NET and is more than capable of handling the project's data requirements.

Key technical challenges have been identified and planned for: multilingual implementation, clinic locator map API integration, deployment environment configuration, and Android device fragmentation for testing. Each challenge has a corresponding mitigation strategy, as documented in the Risk Register (Section 7). The team has access to the necessary development hardware, software licences, version control infrastructure (GitHub), and academic support resources to address these challenges.


9.2 Economic Feasibility

The project is assessed as highly economically feasible for the student development phase. The substantial reliance on in-kind contributions and free tools means the project can be delivered without requiring a dedicated monetary budget from either COSUP or IIE Rosebank College. All required development software is available through student, community, or open-source licences. The only anticipated out-of-pocket costs relate to travel, printing, communication, and initial hosting, all of which are manageable within the team's personal means.


For long-term sustainability post-handover, the platform is economically viable for COSUP provided the organisation makes a modest commitment. Recurring hosting and domain registration costs are estimated at between R500 and R3,000 per year, depending on the provider and traffic levels — a sustainable operational cost for an established organisation. Content updates can be managed by non-technical staff through the admin interface. No recurring software licencing fees will apply, as the platform is built on open-source and free-to-use technologies. A technical point of contact — internal or third-party — will be required for occasional maintenance, and the Maintenance and Handover Guide will equip COSUP to manage this transition effectively.

The total estimated commercial value of equivalent work procured from a professional software development agency ranges from R265,000 to R505,000, encompassing discovery, design, development, project management, quality assurance, and documentation. This figure demonstrates the significant tangible value that this student collaboration delivers to COSUP, with the team's academic credit serving as the sole form of compensation.


WEBSITE (PROTOTYPE)

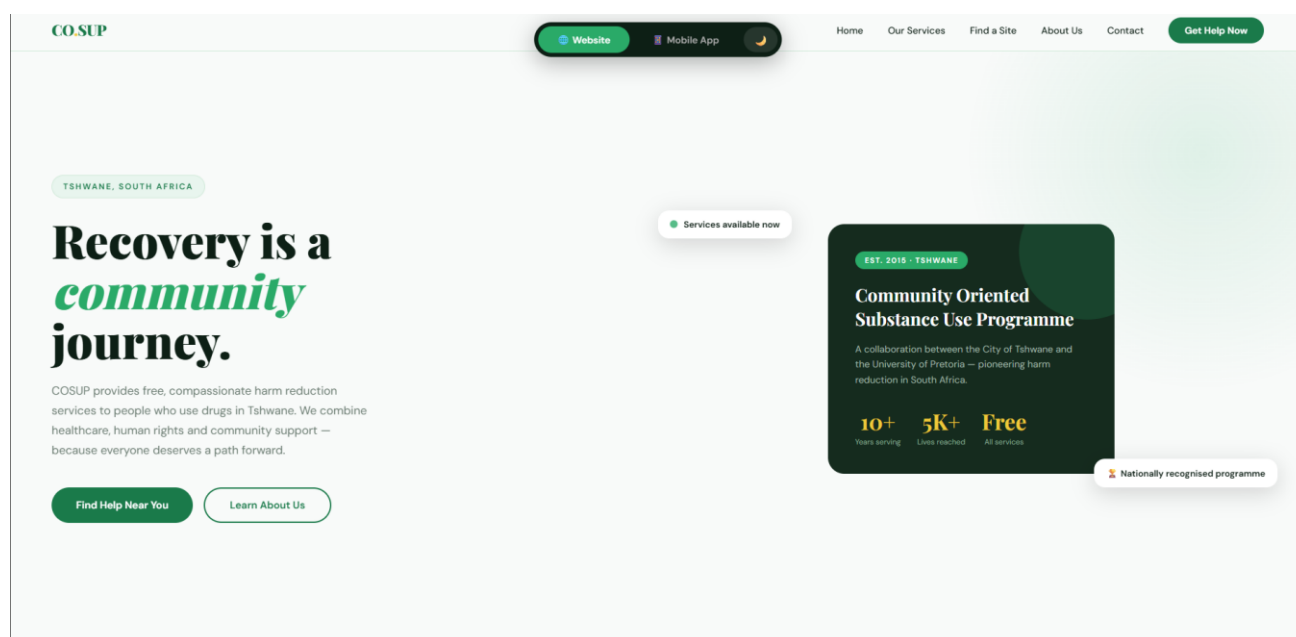


HOME PAGE

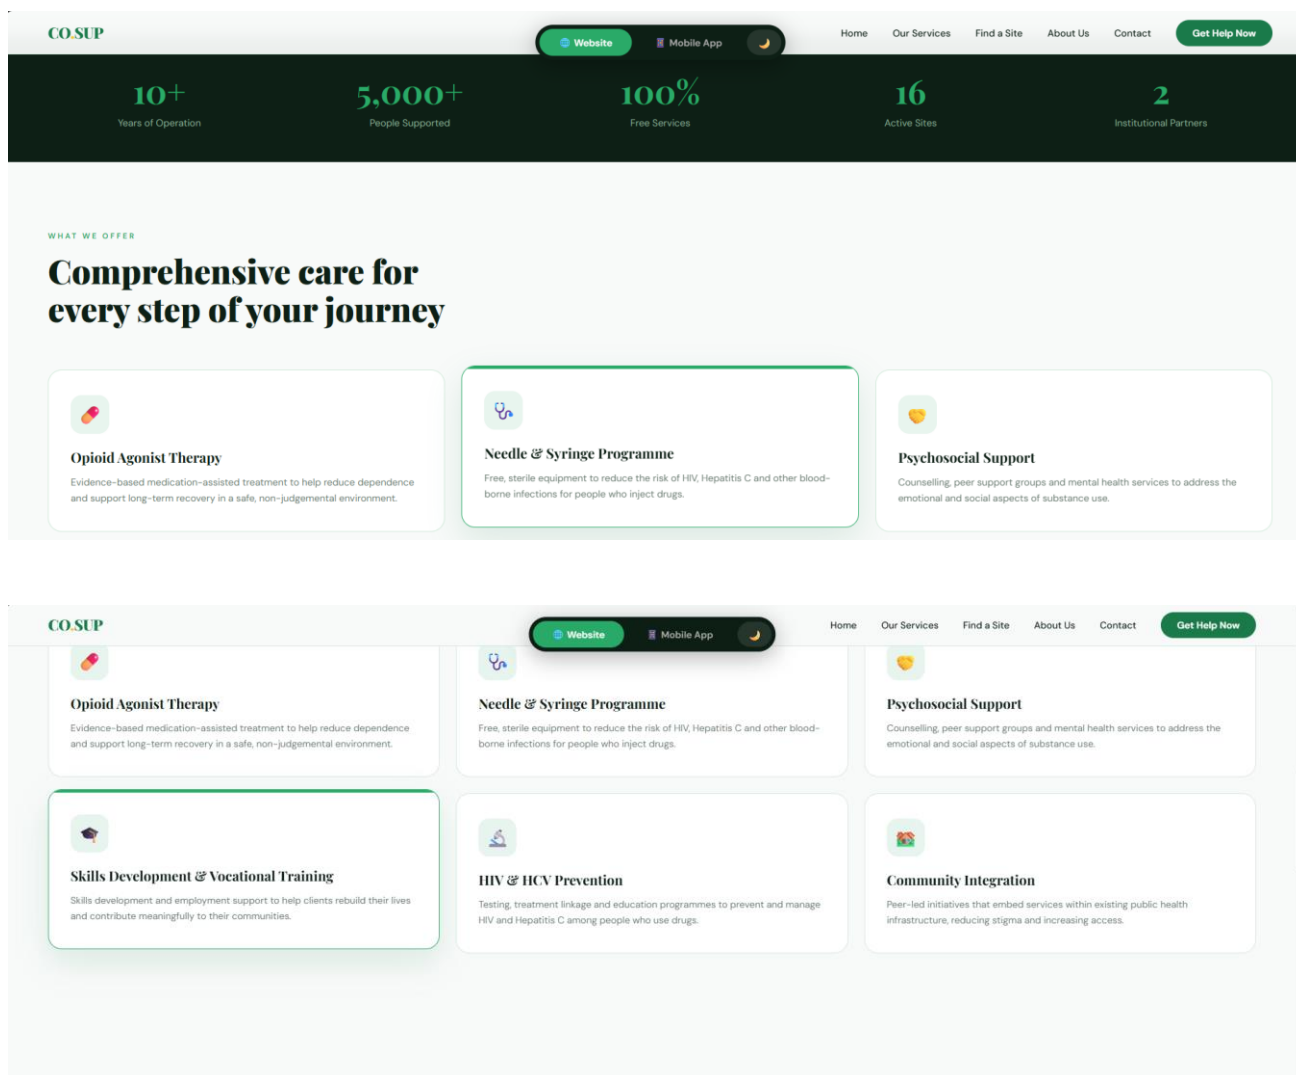


SERVICE PAGE


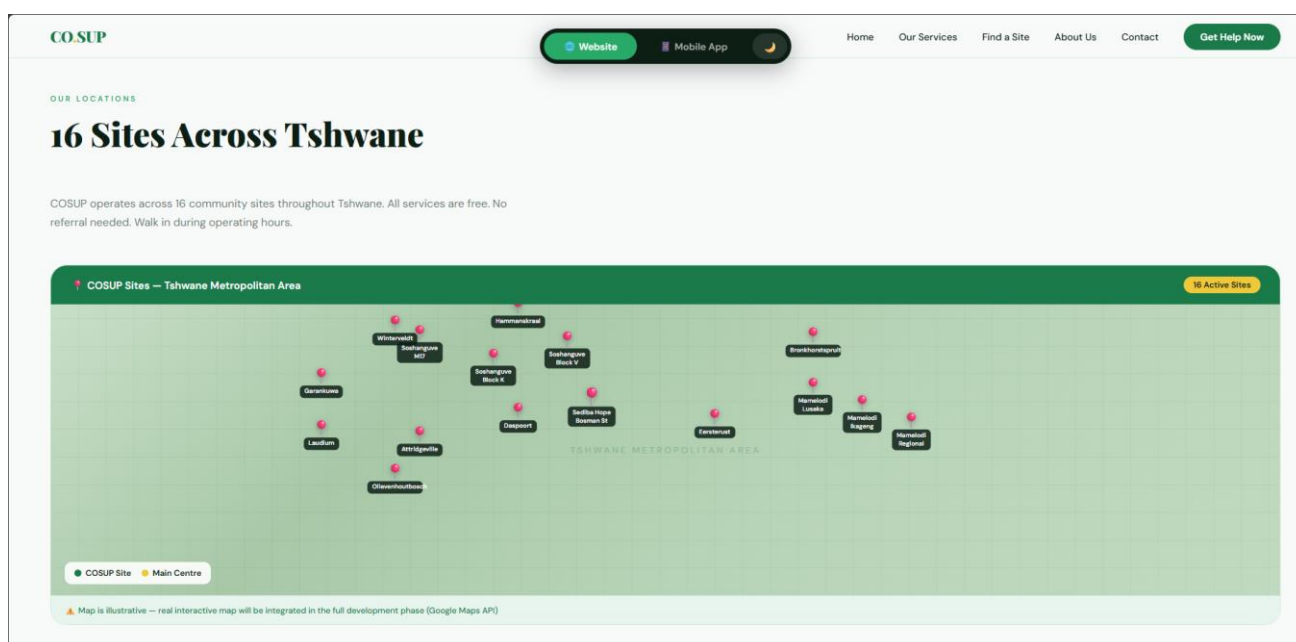


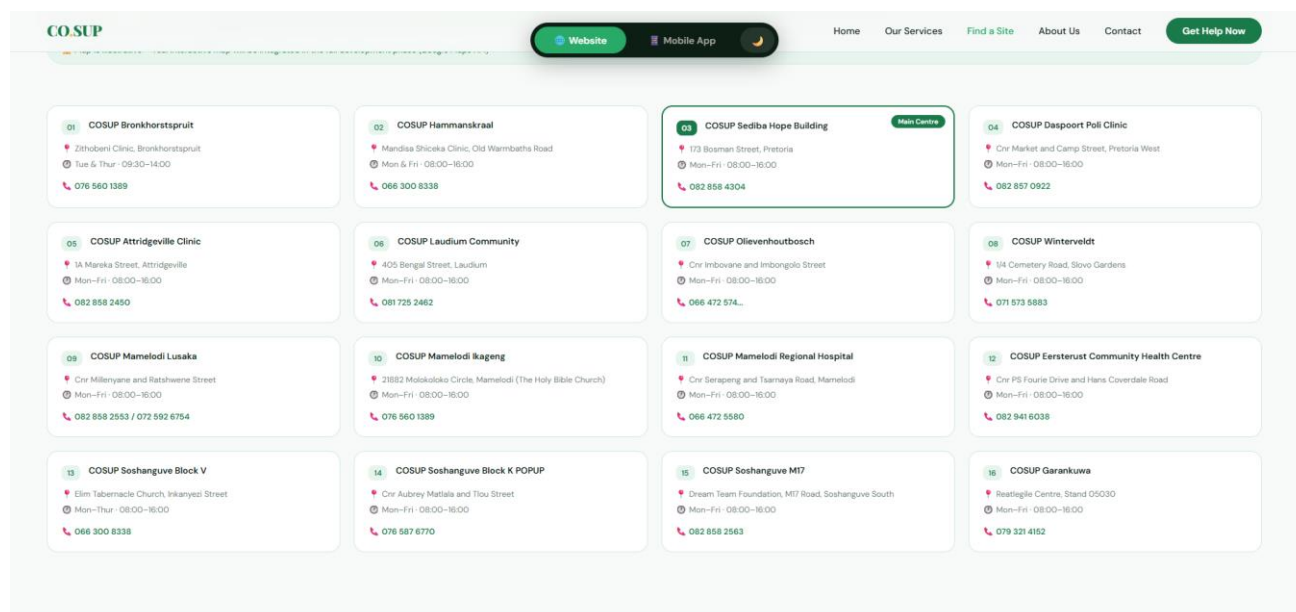

FIND US PAGE


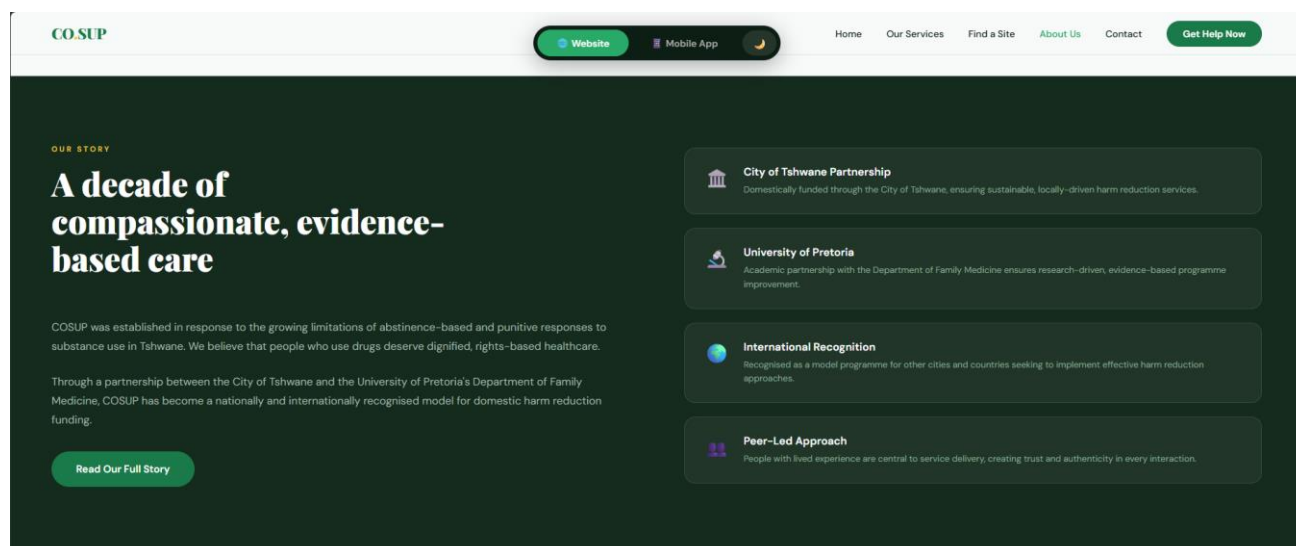


ABOUT US PAGE

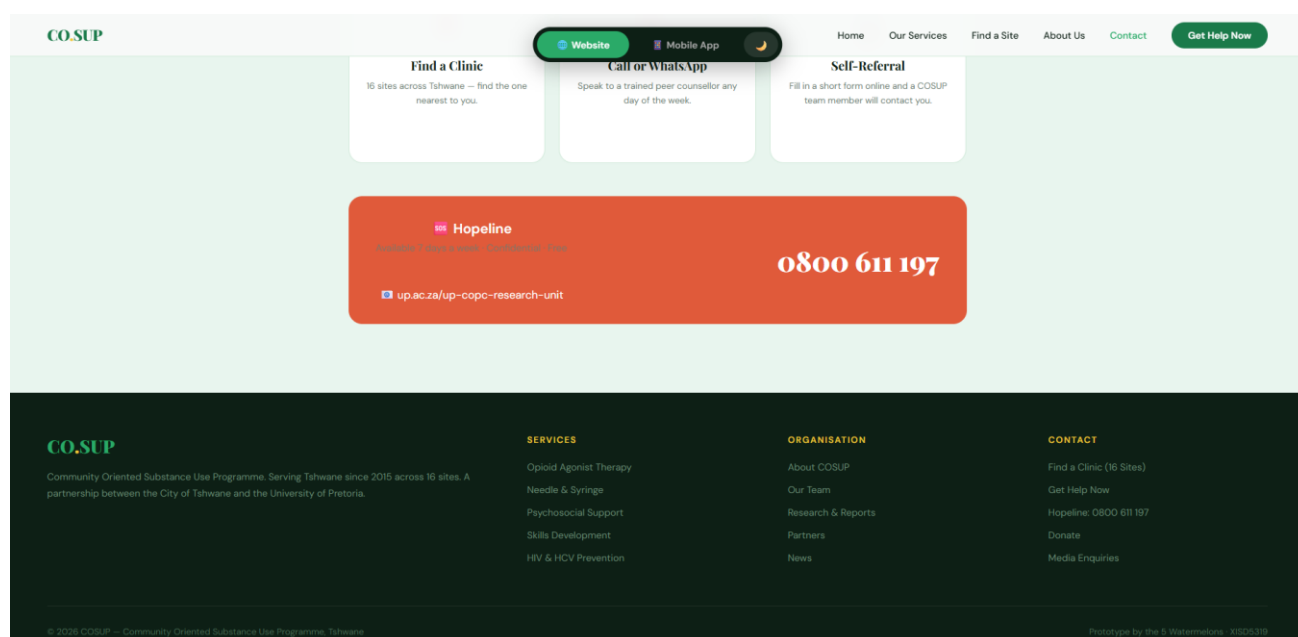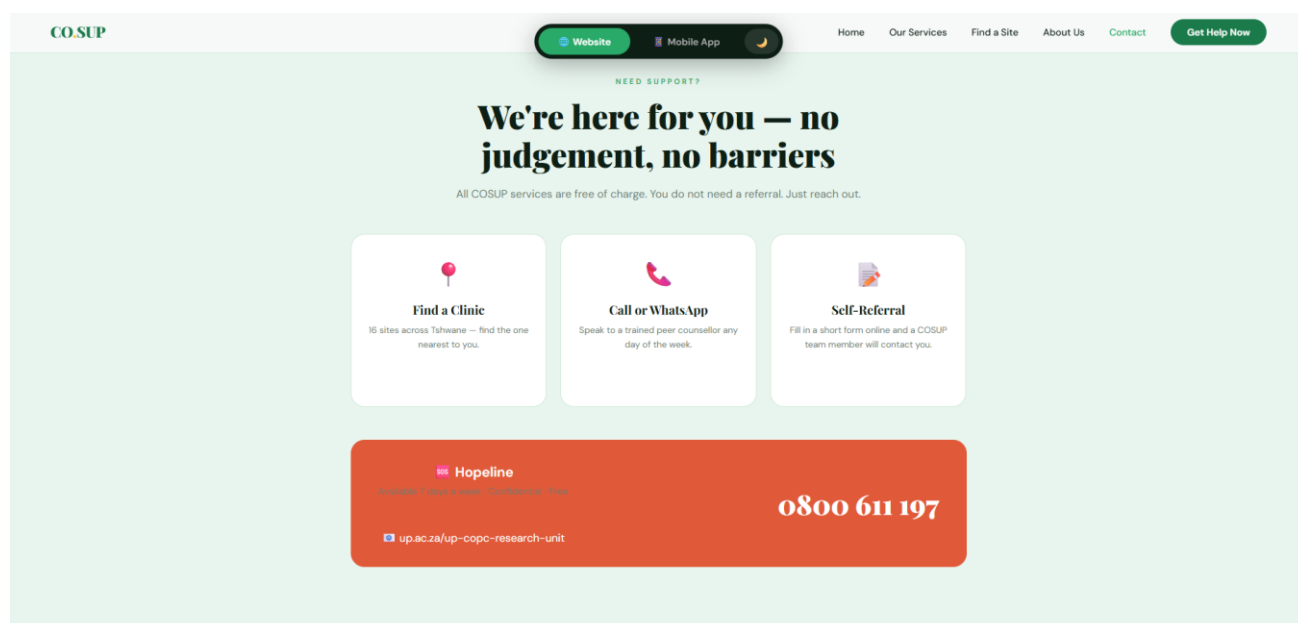

CONTACT PAGE

MOBILE APP (PROTOTYPE)

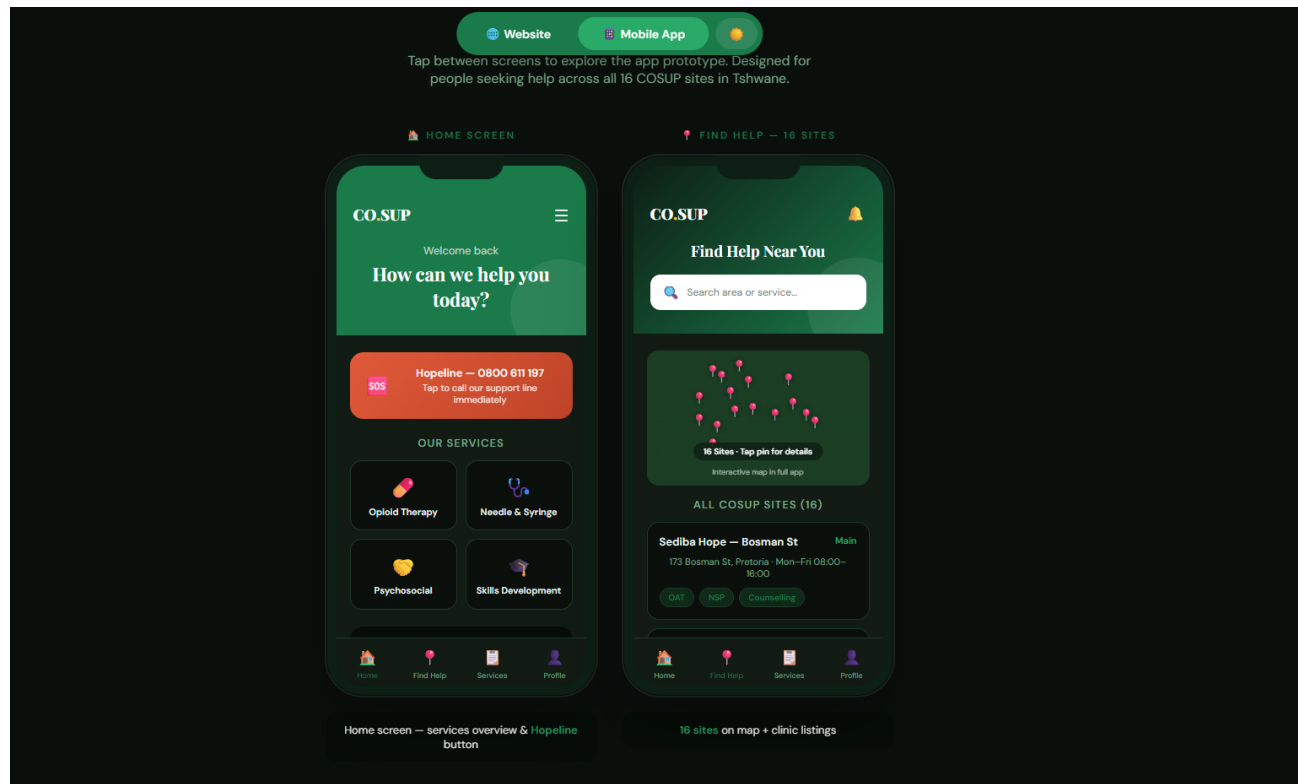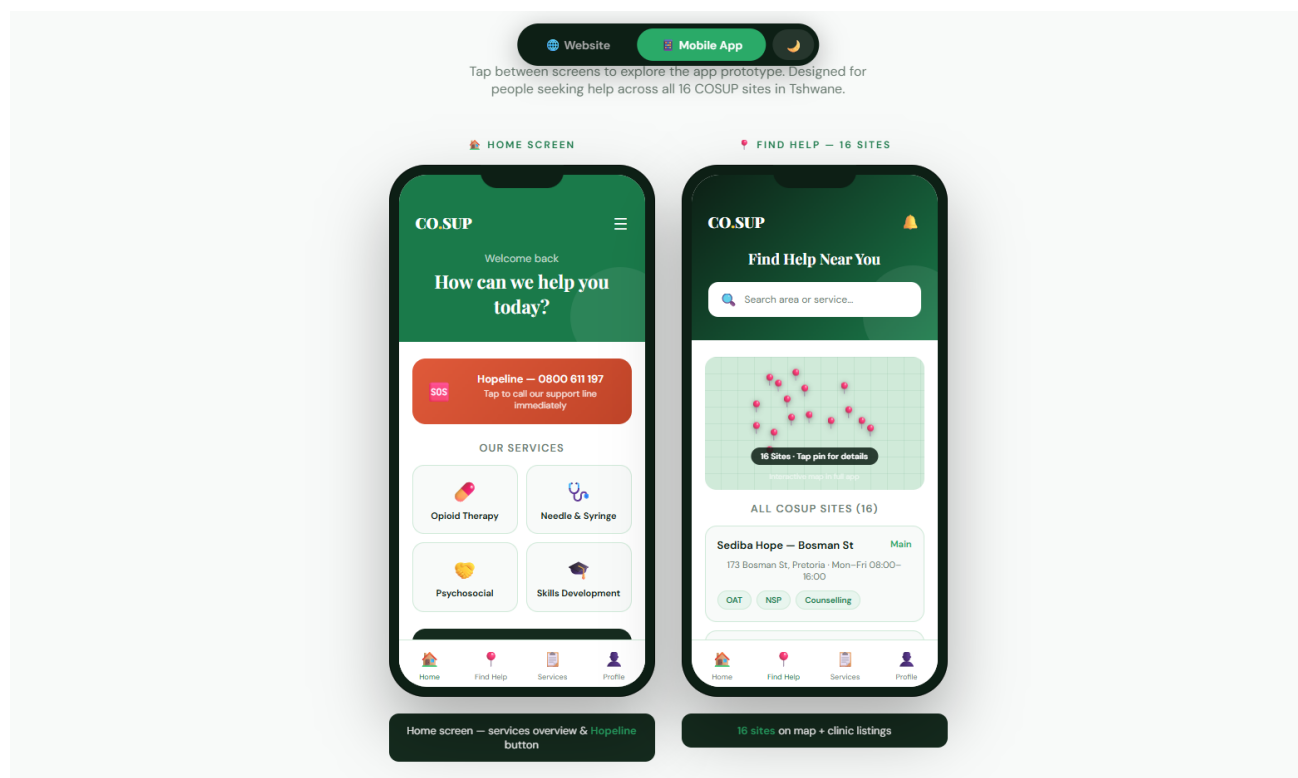

10. Project Organisation

10.1 Roles and Responsibilities

The project is executed by The 5 Watermelons, a five-member student development team enrolled in the XISD5319 Work Integrated Learning module at IIE Rosebank College. The following table defines the roles and primary responsibilities of each team member. Notwithstanding the primary role assignments below, all team members are expected to contribute collaboratively across development, testing, and documentation activities throughout the project lifecycle.

Role	Team Member	Primary Responsibilities
Project Manager	Zandile Selao	Oversees project timeline; facilitates team meetings; manages client and supervisor communications; tracks milestones; ensures on-time delivery.
Business Analyst	Avril Nkuna	Leads ASP.NET MVC and C# development; designs and manages the SQL Server database; develops back-end APIs for the mobile application.
Developer	Tshiamo Mosetlha	Leads Android app development in Kotlin; ensures mobile UI/UX implementation; manages integration with back-end services.
UI/UX Designer	Hope Keebine	Refines the UI/UX prototype; implements website front-end (HTML, CSS, JavaScript); ensures responsive design; leads multilingual interface implementation.
QA Tester	Ndabezinhle Mathunyane	Develops and executes test plans; conducts cross-browser and cross-device testing; tracks bugs; leads creation of the Maintenance and Handover Guide; ensures all documentation is complete.

Academic Supervisor: [Insert Supervisor Name and Title] — IIE Rosebank College. The academic supervisor provides guidance, oversight, and formal evaluation of all project deliverables against the module's academic requirements.

10.2 Stakeholders

Internal Stakeholders

Stakeholder	Role / Interest in the Project
The 5 Watermelons (Student Team)	Responsible for the full design, development, and delivery of the COSUP website and mobile application.
Academic Supervisor	Provides guidance, oversight, and evaluation against the module's academic requirements. Ensures deliverables meet educational standards.

XISD5319 Module Coordinator	Oversees the Work Integrated Learning module; sets and enforces submission deadlines; responsible for final academic assessment.
------------------------------------	--

External Stakeholders

Stakeholder	Role / Interest in the Project
COSUP Management	Primary client. Will own the final product and has a direct interest in ensuring it accurately represents the organisation and serves the community.
COSUP Staff & Peer Counsellors	End-users who may use the platform to inform clients or update content. The Hopeline feature directly supports their crisis response work.
People Who Use Drugs — Tshwane	Ultimate beneficiaries. Their ability to access information and support discreetly is the core problem the platform aims to solve.
City of Tshwane	Founding partner of COSUP with a strategic interest in public health initiatives. The platform supports the City's broader public health goals.
University of Pretoria — Dept. of Family Medicine	Academic partner with an interest in community engagement, research dissemination, and the platform as a model for evidence-based public health technology.
Broader Public & Other NGOs	The public-facing website is accessible to all. Other non-profit organisations may look to COSUP as a model for harm reduction service digitalisation.

COSUP Primary Point of Contact: [Insert Name and Title] — Preferred communication method: [Insert] — Expected response timeframe: [Insert]

11. Project Charter Approval

Project Title: COSUP Website & Mobile Application

Date of Charter: 13 March 2026

Declaration

By signing below, the undersigned parties confirm that they have read, understood, and agree to the contents of this Project Charter. This document formally defines the project scope, objectives, deliverables, assumptions, constraints, and success criteria for the development of the COSUP Website and Mobile Application. All parties acknowledge their roles and responsibilities as outlined in this document and agree to work collaboratively to achieve the project's goals within the defined academic timeline. Any proposed changes to the agreed-upon scope must be formally managed through a change control process and approved by all signing parties.

Role	Printed Name	Signature	Date
Project Manager (On behalf of The 5 Watermelons)	Zandile Selao		
Academic Supervisor (IIE Rosebank College)	MR N Ravuluvulu		
COSUP Client Representative (Community Oriented Substance Use Programme)	MISS Zanele		

— End of Project Charter —
